

IT367 – Software Project Management

LAB 3 – STUDENT SUBMISSION TEMPLATE

Developing a Work Breakdown Structure (WBS) for the Selected Project

A. Group Information

Group No.	1	Project Title	Abhinay: Film Production Networking and Casting Platform
Date	25-08-2026	Project Manager	Ishan Agrawal
Client Representative(s)	Arjun S	Other Management Roles	Happy, Abhishek, Triya, Priyadarshani, Himanshu, Kshitesh, Yuva Raju, Nikitha

B. Project Scope Reference

Abhinay is a film production networking and casting platform that enables professionals from the film industry to create profiles, discover and post casting opportunities, apply for roles, manage applications, communicate, participate in auditions, showcase projects, network with other professionals, and support administrative moderation.

The project scope includes User Management & Profiles, Casting Marketplace, Application Lifecycle Management, Communication & Audition, Project Pages & Networking, and Admin & Moderation.

C. Major Deliverables / Phases

Identify approximately 4–6 major parts of your project.

S. No.	WBS Code	Major Deliverable / Phase
1	1.1	User Management & Profiles
2	1.2	Casting marketplace
3	1.3	Application Lifecycle Management
4	1.4	Communication and Audition
5	1.5	Project Pages and Networking
6	1.6	Admin and Moderation

D. Detailed WBS Hierarchy

Break every major deliverable into smaller work packages/tasks. Add more rows if required.

WBS Code	Deliverable / Work Package / Task	Level	Responsible Role	Output / Completion Criterion
1.0	Abhinay – Film Production Networking & Casting Platform	1	Project Manager	Complete project delivered
1.1	User Management & Profiles	2	Full-stack Team	User and profile management module

1.1.1	User Registration & Authentication	3	Backend Dev	Authentication system implemented
1.1.1.1	Multi-role sign-up (Actor, Director, Producer, Camera Operator, Editor, Other Crew)	4	Backend Dev	Users can register with selected roles
1.1.1.2	Login, logout & role-based access control	4	Backend Dev	Users can securely log in/out and access authorized features
1.1.2	Professional Profile Management	3	Frontend + Backend Dev	Professional profile module
1.1.2.1	Profile creation (skills, experience, bio)	4	Frontend Dev	User can create and update profile details
1.1.2.2	Portfolio / resume-CV upload	4	Backend Dev	Portfolio and resume upload supported
1.1.2.3	Photo & reel upload	4	Backend Dev	Photos and reels can be uploaded
1.2	Casting Marketplace	2	Full-stack Team	Casting marketplace available
1.2.1	Casting Role Posting	3	Backend Dev	Casting role management
1.2.1.1	Create/publish posting (description, requirements, compensation, location)	4	Backend Dev	Role posting can be created and published
1.2.1.2	Edit / close posting	4	Backend Dev	Existing posting can be edited or closed
1.2.2	Role Discovery & Application	3	Frontend Dev	Role discovery and application system
1.2.2.1	Browse & search casting roles	4	Frontend Dev	Users can browse and search roles
1.2.2.2	Apply to a casting role	4	Frontend Dev	Users can submit applications
1.2.3	Shortlist Management	3	Backend Dev	Applicant shortlisting system
1.2.3.1	Create shortlist folders	4	Backend Dev	Named shortlist folders can be created
1.2.3.2	Organize applicants into folders	4	Backend Dev	Applicants can be organized into folders
1.3	Application Lifecycle Management	2	Backend Dev	Application management module

1.3.1	Applicant Review Dashboard	3	Frontend Dev	Applicant review interface
1.3.1.1	View applicants per posting	4	Frontend Dev	Applicants displayed for each posting
1.3.2	Application Status Tracking	3	Backend Dev	Application status management
1.3.2.1	Update status (Applied / Shortlisted / Selected / Rejected)	4	Backend Dev	Application status updates correctly
1.3.2.2	Notify applicant on status change	4	Backend Dev	Applicant receives status notification
1.4	Communication & Audition	2	Full-stack Team	Communication and audition features
1.4.1	Direct Messaging	3	Backend Dev	Messaging functionality
1.4.1.1	Send / receive messages	4	Backend Dev	Users can exchange messages
1.4.1.2	Message inbox UI	4	Frontend Dev	Message inbox interface available
1.4.2	Scheduled Audition / Screening	3	Backend Dev	Audition scheduling system
1.4.2.1	Schedule audition session	4	Backend Dev	Audition sessions can be scheduled
1.4.2.2	Real-time communication during session	4	Backend Dev	Real-time communication supported
1.4.3	Self-Tape Submission	3	Backend Dev	Self-tape submission system
1.4.3.1	Upload video resume / self-tape	4	Backend Dev	Video resume/self-tape can be uploaded
1.4.3.2	Secure media storage & streaming	4	Backend Dev	Uploaded media stored securely
1.5	Project Pages & Networking	2	Full-stack Team	Project and networking features
1.5.1	Project Page Management	3	Frontend + Backend Dev	Project page module
1.5.1.1	Create film/show project page	4	Frontend Dev	Project page can be created
1.5.2.1	Link crew profiles to their projects	4	Backend Dev	Crew profiles display associated projects
1.5.3	Social Networking Feed	3	Frontend Dev	Professional networking feed
1.5.3.1	Connect / follow other professionals	4	Frontend Dev	Users can connect and follow others
1.5.3.2	Industry/project post feed	4	Frontend Dev	Users can view industry and project posts
1.6	Admin & Moderation	2	Backend Dev	Administrative management module
1.6.1	Admin Dashboard	3	Backend Dev	Admin dashboard
1.6.1.1	User/post moderation tools	4	Backend Dev	Admin can moderate users and posts


1.6.1.2	Credit verification	4	Backend Dev	Admin can verify user credits
1.6.1.3	User report handling	4	Backend Dev	Admin can handle and resolve reports

E. WBS Dictionary – Major Work Packages

Choose at least 4 important work packages from Section D and explain them briefly.

WBS Code	Work Package	What work is included?	Expected Output	How will you know it is complete?
1.1.1	User Registration & Authentication	Multi-role registration, login, logout and role-based access control	Working sign-up and login system	Users can register, select a role, log in, log out and access authorized features
1.2.1	Casting Role Posting	Create, publish, edit and close casting role postings	Published casting role listing	Producer/director can create, edit and publish a role visible to applicants
1.2.2	Role Discovery & Application	Browse, search and apply to available casting roles	Searchable role listing and application feature	Actor/crew can search for roles and successfully submit an application
1.3.2	Application Status Tracking	Manage application states and notify applicants about status changes	Application status tracking system	Status correctly changes between Applied, Shortlisted, Selected and Rejected
1.4.1	Direct Messaging	Send and receive messages and provide message inbox	Chat/inbox feature	Two users can successfully exchange messages
1.5.1	Project Page Management	Create project pages and attach cast and crew	Project profile page	Project page displays project details and linked cast/crew

F. Optional WBS Tree / Hierarchy Diagram

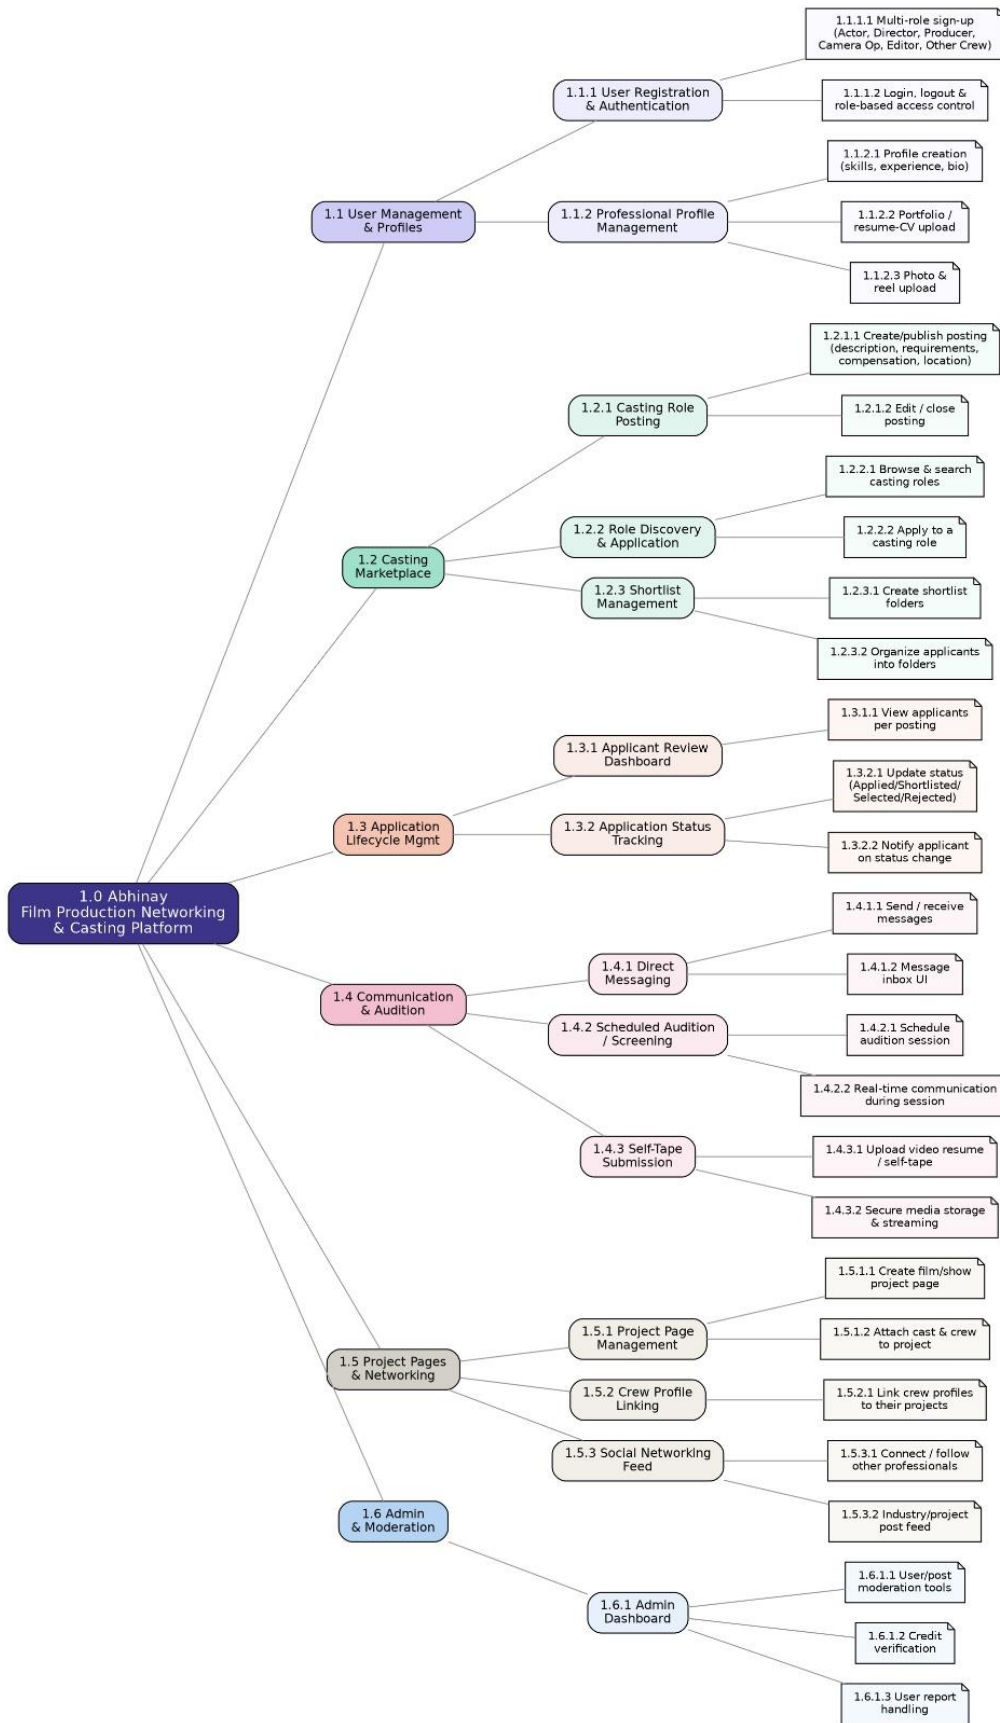

G. Client & Project Manager Review

Review Question	Answer	Correction / Comment
1. Is all approved project work included?	Yes	All six approved major functional areas are included in the WBS.
2. Is any work repeated in two places?	No	Each task has been assigned to one primary work package to avoid duplication.
3. Is anything outside the approved scope included?	No	The WBS only contains work related to the approved project scope.
4. Are the work packages small and clear enough to assign and check?	Yes	Major deliverables have been broken down into smaller, assignable tasks with responsible roles and completion criteria.

H. Final Reflection

The most difficult work package to break into smaller parts was **Communication & Audition**. This was challenging because it contains several technically different features, including direct messaging, audition scheduling, real-time communication, and self-tape submission.

These features require different frontend, backend, real-time communication, and media-handling components. Therefore, extra care was needed to divide the work into clear and non-overlapping work packages.

I. Submission Checklist

- ☐ Same project and approved scope from Lab 2 used.
- ☐ 4–6 major deliverables/phases identified.
- ☐ Major deliverables broken into smaller work packages/tasks.
- ☐ WBS codes included.
- ☐ Responsible roles included.
- ☐ Outputs and completion criteria included.
- ☐ WBS dictionary completed for important work packages.
- ☐ WBS reviewed by client representative(s) and Project Manager.
- ☐ One completed document is being submitted for the group.

J. Sign-off

Project Manager Name / Signature	Ishan Agrawal
Client Representative Name / Signature	Arjun S
Date	25-08-2026

Keep this Lab 3 output safely. It will be used in later project-management activities.
